


Owner: Town of Nantucket  
 GC: Robert B. Our Co., Inc.  
 Engineer: Environmental Partners

Sea Street Pump Station- Force Main No. 3  
 Town of Nantucket  
 CWSRD#6722  
 Construction Schedule  
 2/15/22



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	July	December	May	October	March	August	January	June	November	April	September	February	July
							M	E	B	M	E	B	M	E	B	M	E	B	M
0		<b>Sea Street Pump Station- Force Main No. 3</b>	<b>852 days</b>	<b>Thu 10/28/21</b>	<b>Mon 3/31/25</b>														
1		Contract Award	0 days	Thu 10/28/21	Thu 10/28/21														
2		<b>Contract Notice to Proceed (TBD)</b>	0 days	Fri 4/1/22	Fri 4/1/22	1FS+109 days													
3		Substantial Completion (1,035 days > NTP)	0 days	Thu 1/30/25	Thu 1/30/25	2SS+1035 edays													
4		Final Completion (1,095 days > NTP)	0 days	Mon 3/31/25	Mon 3/31/25	2SS+1095 edays													
5		Layout	5 days	Mon 4/4/22	Fri 4/8/22	2													
6		Mobilize	3 days	Mon 4/4/22	Wed 4/6/22	2													
7		Erosion Control- Season 1	2 days	Mon 4/4/22	Tue 4/5/22	2													
8		Erosion Control- Season 2	2 days	Mon 10/3/22	Tue 10/4/22														
9		Erosion Control- Season 3	2 days	Mon 9/16/24	Tue 9/17/24														
10		Excavate & Backfill Test Pits Phase 1	10 days	Mon 4/4/22	Fri 4/15/22	7SS													
11		<b>South Shore Road</b>	<b>159 days</b>	<b>Mon 4/11/22</b>	<b>Wed 11/30/22</b>														
12		<b>STA 183+60 - STA 179+25</b>	<b>22 days</b>	<b>Mon 4/11/22</b>	<b>Wed 5/11/22</b>														
13		Furnish and Install Force Main	20 days	Mon 4/11/22	Mon 5/9/22	2FS+5 days													
14		Pressure Test Force Main	2 days	Tue 5/10/22	Wed 5/11/22	13													
15		<b>STA 154+47 (IAMH7) - STA 126+40 (IAMH6)</b>	<b>22 days</b>	<b>Thu 5/12/22</b>	<b>Mon 6/13/22</b>														
16		Furnish and Install Force Main	20 days	Thu 5/12/22	Thu 6/9/22	14													
17		Pressure Test Force Main	2 days	Fri 6/10/22	Mon 6/13/22	16													
18		<b>STA 126+40 (IAMH6) - STA 124+00</b>	<b>115 days</b>	<b>Tue 6/14/22</b>	<b>Wed 11/30/22</b>														
19		Furnish and Install Force Main	3 days	Tue 6/14/22	Thu 6/16/22	17													
20		Pressure Test Force Main	1 day	Fri 6/17/22	Fri 6/17/22	19													
21		Final Pavement: Grade & Pave Binder	7 days	Tue 6/21/22	Wed 6/29/22	20													
22		Final Pavement- Top	3 days	Mon 11/28/22	Wed 11/30/22	21FS+101 days													
23		<b>Surfside Road</b>	<b>200 days</b>	<b>Mon 9/12/22</b>	<b>Fri 6/30/23</b>														
24		<b>STA 124+00 - STA 112+43 (ARV5)</b>	<b>59 days</b>	<b>Mon 9/12/22</b>	<b>Wed 12/7/22</b>														
25		Furnish and Install Force Main	20 days	Mon 9/12/22	Fri 10/7/22														
26		Pressure Test Force Main	3 days	Mon 12/5/22	Wed 12/7/22														
27		Furnish and Install Force Main Check Valve	2 days	Thu 12/1/22	Fri 12/2/22														
28		<b>STA 112+43 (ARV5) - STA 90+14 (ARV4)</b>	<b>43 days</b>	<b>Tue 10/11/22</b>	<b>Tue 12/13/22</b>														
29		Furnish and Install Force Main	30 days	Tue 10/11/22	Tue 11/22/22	25													
30		Pressure Test Force Main	4 days	Thu 12/8/22	Tue 12/13/22	26													
31		Furnish and Install IAMH-4A + 5A Cross Connect	5 days	Wed 11/23/22	Thu 12/1/22	29													

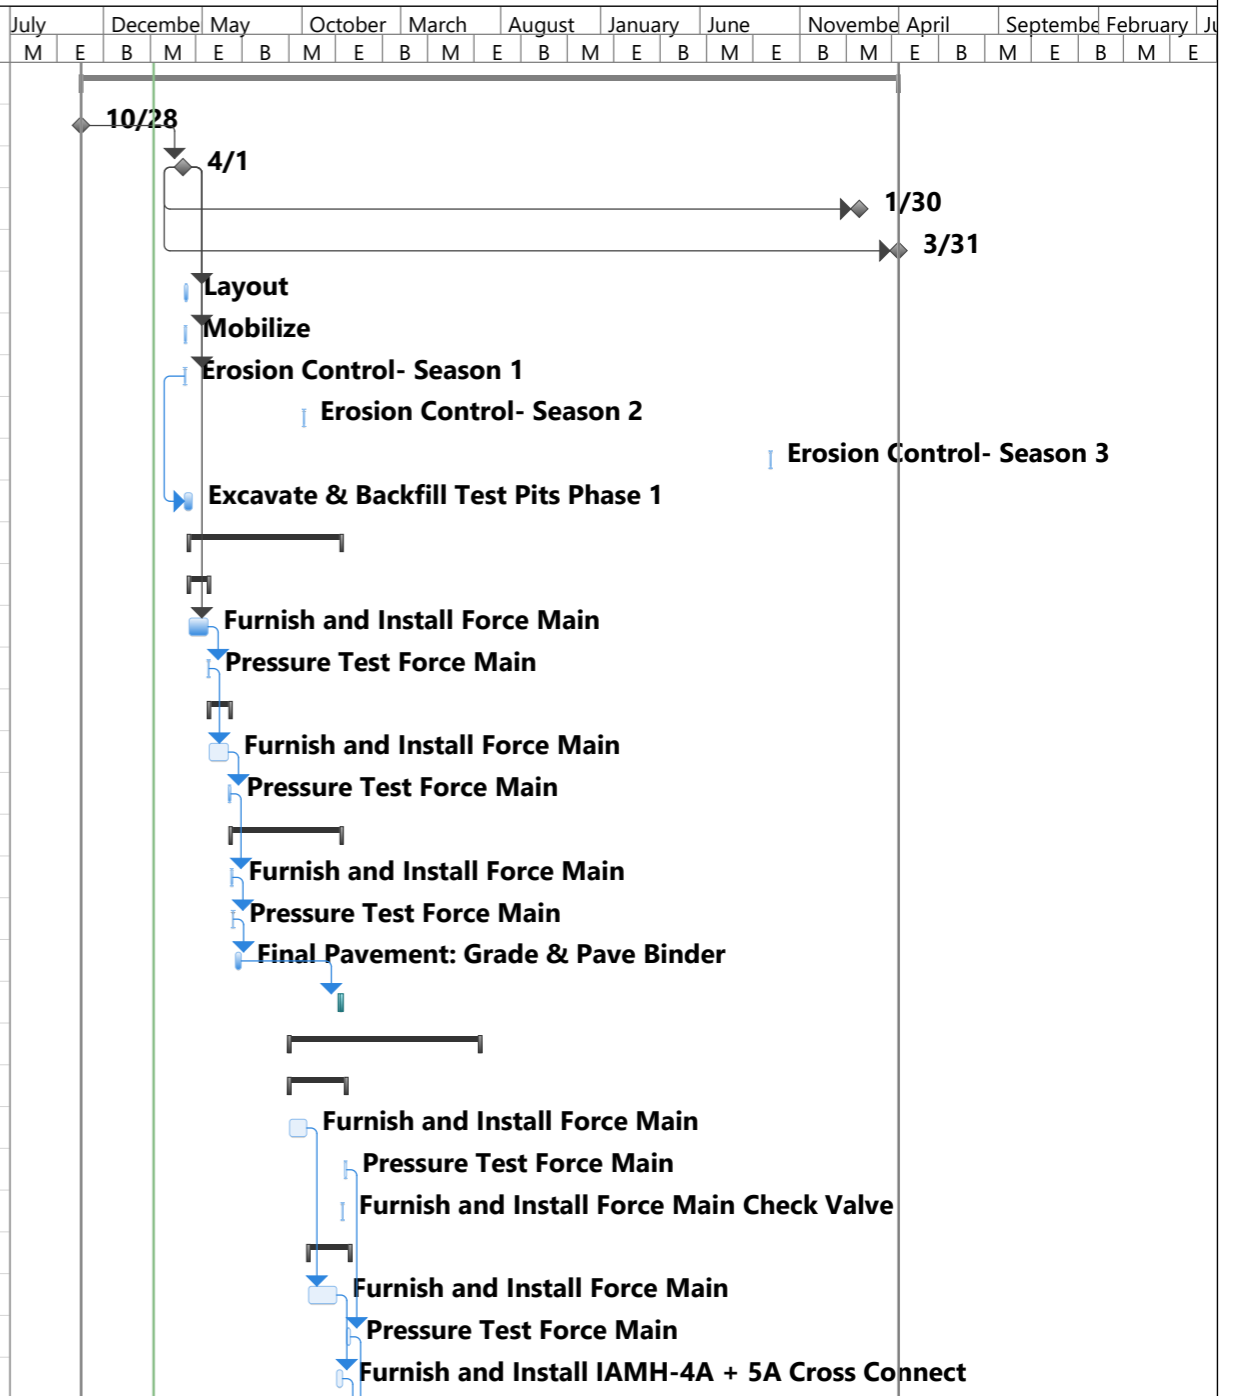

Project: Sea Street Pump Station  
 Date: Wed 2/16/22


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Owner: Town of Nantucket  
 GC: Robert B. Our Co., Inc.  
 Engineer: Environmental Partners

Sea Street Pump Station- Force Main No. 3  
 Town of Nantucket  
 CWSRD#6722  
 Construction Schedule  
 2/15/22



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar																						
							July	December	May	October	March	August	January	June	November	April	September	February	July										
							M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E
32		<b>STA 90+14 (ARV-4) - STA 81+69 (IAMH-3)</b>	<b>10 days</b>	<b>Fri 12/2/22</b>	<b>Thu 12/15/22</b>																								
33		Furnish and Install Force Main	10 days	Fri 12/2/22	Thu 12/15/22	31																							
34		Pressure Test Force Main	2 days	Wed 12/14/22	Thu 12/15/22	30																							
35		<b>STA 81+69 (IAMH-3) - STA 58+22 (ARV3)</b>	<b>135 days</b>	<b>Fri 12/16/22</b>	<b>Fri 6/30/23</b>																								
36		Furnish and Install Force Main	30 days	Fri 12/16/22	Tue 1/31/23	33																							
37		Pressure Test Force Main	4 days	Fri 12/16/22	Wed 12/21/22	34																							
38		Furnish and Install Drainage	3 days	Wed 2/1/23	Fri 2/3/23	36																							
39		Final Pavement: Bike Path Restoration/ Installation (#86 Surfside to Fairgrounds Rd)	10 days	Mon 6/5/23	Fri 6/16/23																								
40		Final Pavement: Permanent Trench Patch (Sparks Ave to # 86 Surfside Rd)	10 days	Mon 6/19/23	Fri 6/30/23	39																							
41		<b>Atlantic Avenue</b>	<b>57 days</b>	<b>Mon 4/3/23</b>	<b>Thu 6/22/23</b>																								
42		<b>STA 58+22 (ARV3) - STA 56+00</b>	<b>57 days</b>	<b>Mon 4/3/23</b>	<b>Thu 6/22/23</b>																								
43		Furnish and Install Gravity Sewer	4 days	Mon 4/3/23	Thu 4/6/23																								
44		Remove and Dispose of Fire Cistern	1 day	Fri 4/7/23	Fri 4/7/23	45SS-1 day																							
45		Furnish and Install Force Main	5 days	Mon 4/10/23	Fri 4/14/23	43FS+1 day																							
46		Furnish and Install Drainage	5 days	Tue 4/18/23	Mon 4/24/23	45																							
47		Pressure Test Force Main	2 days	Tue 5/23/23	Wed 5/24/23	45FS+25 days																							
48		Furnish and Install Verticle Granite Curb	2 days	Mon 6/5/23	Tue 6/6/23																								
49		Furnish and Install Brick Sidewalk	7 days	Wed 6/7/23	Thu 6/15/23	48																							
50		Final Pavement: Furnish and Install Reclaim & Pave	5 days	Fri 6/16/23	Thu 6/22/23	49																							
51		<b>Pleasant Street</b>	<b>40 days</b>	<b>Tue 4/25/23</b>	<b>Tue 6/20/23</b>																								
52		<b>STA 56+00 - STA 52+25</b>	<b>40 days</b>	<b>Tue 4/25/23</b>	<b>Tue 6/20/23</b>																								
53		Furnish and Install Force Main	5 days	Tue 4/25/23	Mon 5/1/23	46																							
54		Pressure Tet Force Main	2 days	Thu 5/25/23	Fri 5/26/23	47																							
55		Furnish and Install Verticle Granite Curbing	2 days	Wed 6/7/23	Thu 6/8/23																								
56		Final Pavement: Furnish and Install Trench Patch	2 days	Mon 6/19/23	Tue 6/20/23	55FS+6 days																							
57		<b>Silver Street</b>	<b>38 days</b>	<b>Tue 5/2/23</b>	<b>Fri 6/23/23</b>																								
58		<b>STA 52+25 - STA 50+50</b>	<b>38 days</b>	<b>Tue 5/2/23</b>	<b>Fri 6/23/23</b>																								
59		Furnish and Install Gravity Sewer	5 days	Tue 5/2/23	Mon 5/8/23	53																							
60		Furnish and Install Force Main	5 days	Tue 5/9/23	Mon 5/15/23	59																							

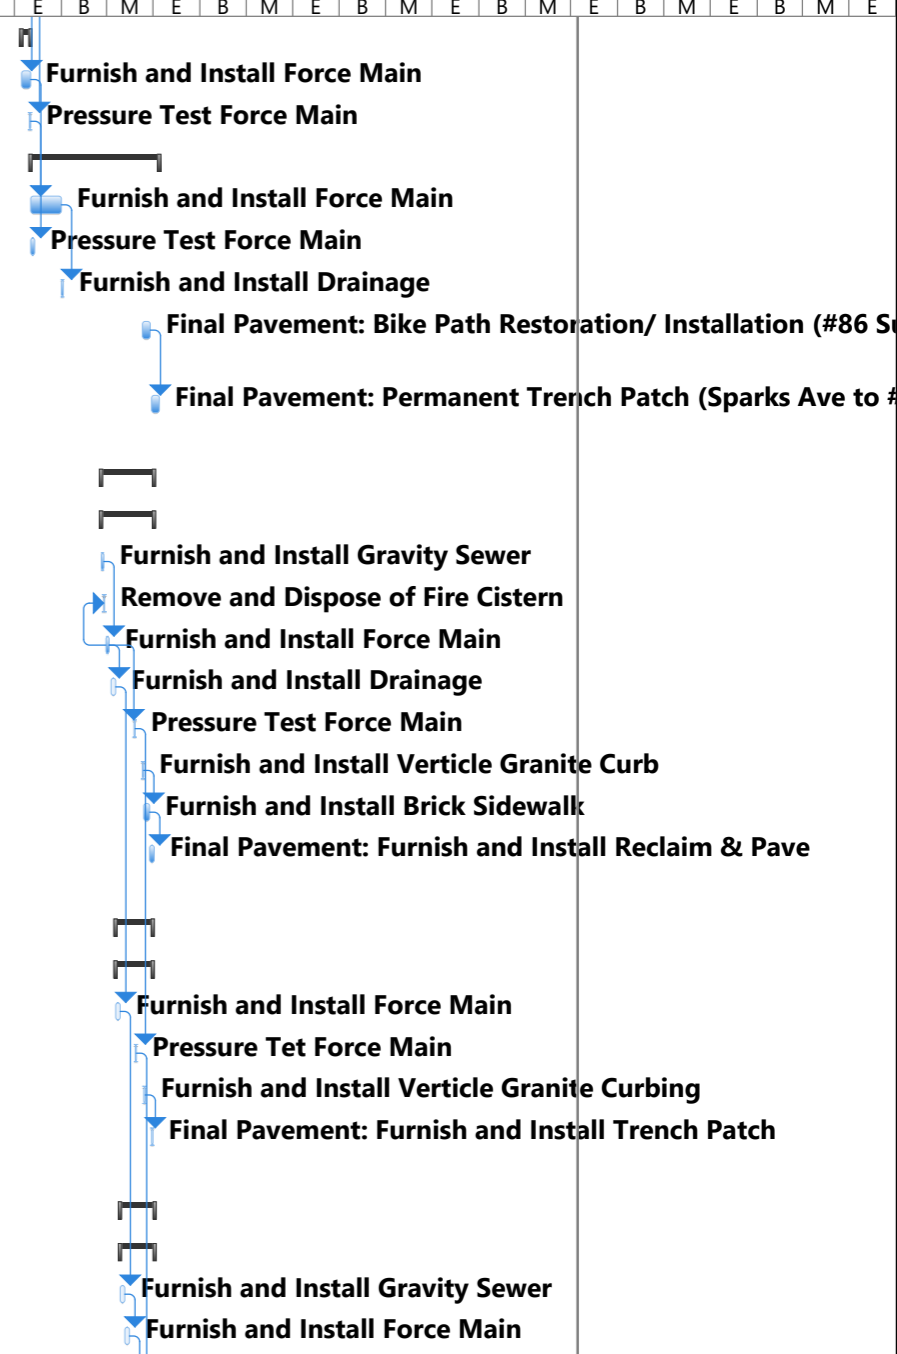

Project: Sea Street Pump Statio  
 Date: Wed 2/16/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Month																
							July	December	May	October	March	August	January	June	November	April	September	February	July				
61	↳	Pressure Test Force Main	2 days	Tue 5/30/23	Wed 5/31/23	54																	
62	↳	Furnish and Install Watermain	3 days	Tue 5/16/23	Thu 5/18/23	60																	
63	↳	Furnish and Install Drainage	5 days	Fri 5/19/23	Thu 5/25/23	62																	
64	↳	Furnish and Install Water Services	2 days	Fri 5/26/23	Tue 5/30/23	63																	
65	↳	Final Pavement: Full Depth Reclamation and Repave	5 days	Mon 6/19/23	Fri 6/23/23																		
66	↳	<b>Pine Street</b>	<b>122 days</b>	<b>Tue 11/14/23</b>	<b>Fri 5/10/24</b>																		
67	↳	<b>STA 50+50 - STA 33+50</b>	<b>122 days</b>	<b>Tue 11/14/23</b>	<b>Fri 5/10/24</b>																		
68	↳	Furnish and Install Gravity Sewer	20 days	Tue 11/14/23	Wed 12/13/23	80																	
69	↳	Furnish and Install Force Main	30 days	Thu 12/14/23	Mon 1/29/24	68																	
70	↳	Furnish and Install Watermain	10 days	Tue 1/30/24	Mon 2/12/24	69																	
71	↳	Furnish and Install Water Services	5 days	Tue 2/13/24	Tue 2/20/24	70																	
72	↳	Pressure Test Force Main	5 days	Wed 2/21/24	Tue 2/27/24	70FS+5 days																	
73	↳	Pressure Test + Chlorinate Watermain	2 days	Wed 2/28/24	Thu 2/29/24	72																	
74	↳	Final Pavement: Full Depth Reclamatin and Repave	5 days	Mon 5/6/24	Fri 5/10/24																		
75	↳	<b>Winter Street</b>	<b>56 days</b>	<b>Mon 10/2/23</b>	<b>Fri 12/22/23</b>																		
76	↳	<b>STA 33+50 - STA 30+00</b>	<b>56 days</b>	<b>Mon 10/2/23</b>	<b>Fri 12/22/23</b>																		
77	↳	Furnish and Install Gravity Sewer Main	7 days	Mon 10/2/23	Wed 10/11/23																		
78	↳	Furnish and Install Force Main	15 days	Thu 10/12/23	Wed 11/1/23	77																	
79	↳	Furnish & Install Watermain	5 days	Thu 11/2/23	Wed 11/8/23	78																	
80	↳	Furnish and Install Water Services	2 days	Thu 11/9/23	Mon 11/13/23	79																	
81	↳	Pressure Test Force Main	2 days	Fri 11/17/23	Mon 11/20/23	79FS+5 days																	
82	↳	Pressure Test & Chloriante Watermain	2 days	Tue 11/21/23	Wed 11/22/23	81																	
83	↳	Final Pavement: Install Cobble Stone Pavers	20 days	Mon 11/27/23	Fri 12/22/23																		
84	↳	<b>Liberty Street</b>	<b>88 days</b>	<b>Mon 2/6/23</b>	<b>Mon 6/12/23</b>																		
85	↳	<b>STA 30+00 - STA 21+50</b>	<b>88 days</b>	<b>Mon 2/6/23</b>	<b>Mon 6/12/23</b>																		
86	↳	Furnish and Install Watermain bypass	10 days	Mon 2/6/23	Fri 2/17/23																		
87	↳	Furnish and Install Gravity Sewer	15 days	Tue 2/21/23	Mon 3/13/23	86																	
88	↳	Furnish and Install Force Main	20 days	Tue 3/14/23	Mon 4/10/23	87																	
89	↳	Furnish and Install Watermain	10 days	Tue 4/11/23	Tue 4/25/23	88																	
90	↳	Furnish and Install Drainage	7 days	Wed 4/26/23	Thu 5/4/23	89																	

Project: Sea Street Pump Statio  
 Date: Wed 2/16/22


Task		Project Summary		Inactive Task		Duration-only		Finish-only		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Start-only		Deadline		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress		External Milestone		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone		Manual Progress		External Milestone		Manual Progress	

Owner: Town of Nantucket  
 GC: Robert B. Our Co., Inc.  
 Engineer: Environmental Partners

Sea Street Pump Station- Force Main No. 3  
 Town of Nantucket  
 CWSRD#6722  
 Construction Schedule  
 2/15/22



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar																				
							July	December	May	October	March	August	January	June	November	April	September	February									
							M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	
91		Furnish and Install Water Services	5 days	Fri 5/5/23	Thu 5/11/23	90																					
92		Pressure Test Force Main	5 days	Mon 5/22/23	Fri 5/26/23	88FS+28 days																					
93		Pressure Test & Chlorinate Watermain	5 days	Tue 5/30/23	Mon 6/5/23	92																					
94		Final Pavement: Full Depth Reclamation and Repave	1 day	Mon 6/12/23	Mon 6/12/23	93FS+4 days																					
95		<b>Lilly Street</b>	<b>152 days</b>	<b>Mon 10/17/22</b>	<b>Fri 5/26/23</b>																						
96		<b>STA 21+50 - STA 5+50</b>	<b>152 days</b>	<b>Mon 10/17/22</b>	<b>Fri 5/26/23</b>																						
97		Furnish and Install Watermain Bypass	15 days	Mon 10/17/22	Fri 11/4/22																						
98		Furnish and Install Gravity Sewer	16 days	Mon 11/28/22	Mon 12/19/22	114																					
99		Furnish and Install Force Main	20 days	Tue 12/20/22	Thu 1/19/23	98																					
100		Furnish and Install Watermain	12 days	Fri 1/20/23	Mon 2/6/23	99																					
101		Furnish and Install Services	5 days	Tue 2/7/23	Mon 2/13/23	100																					
102		Furnish and Install Drainage	5 days	Tue 2/14/23	Tue 2/21/23	101																					
103		Pressure Test Force Main	5 days	Fri 2/17/23	Fri 2/24/23	98FS+40 days																					
104		Pressure Test & Chlorinate Watermain	3 days	Mon 2/27/23	Wed 3/1/23	103																					
105		Furnish and Install Verticle Granite Curb and Wheel Chair Ramps	10 days	Mon 5/1/23	Fri 5/12/23																						
106		Final Pavement: Full Depth Reclamation and Repave	10 days	Mon 5/15/23	Fri 5/26/23	105																					
107		<b>Sea Street/ Step Lane</b>	<b>820 days</b>	<b>Mon 12/13/21</b>	<b>Mon 3/31/25</b>																						
108		<b>STA 5+50 - STA 0+00</b>	<b>244 days</b>	<b>Mon 12/13/21</b>	<b>Mon 12/5/22</b>																						
109		Furnish and Install Watermain Bypass	10 days	Mon 10/3/22	Mon 10/17/22																						
110		Furnish and Install Gravity Sewer	15 days	Tue 10/18/22	Mon 11/7/22	109																					
111		Furnish and Install Services	2 days	Tue 11/8/22	Wed 11/9/22	110																					
112		Furnish and Install Force Main	6 days	Thu 11/10/22	Fri 11/18/22	111																					
113		Pressure Test Force Main	2 days	Wed 11/30/22	Thu 12/1/22	112FS+5 days																					
114		Furnish and Install Watermain	3 days	Mon 11/21/22	Wed 11/23/22	112																					
115		Pressure Test & Chlorinate Watermain	2 days	Fri 12/2/22	Mon 12/5/22	113																					
116		Furnish and Install Verticle Granite Curbing	5 days	Mon 12/13/21	Fri 12/17/21																						
117		Remove & Reset Block Pavers at N. Water Street Intersection	30 days	Mon 12/20/21	Tue 2/1/22	116																					
118		Final Pavement: Full Depth Reclamation and Repave	10 days	Tue 5/10/22	Mon 5/23/22	117FS+67 days																					

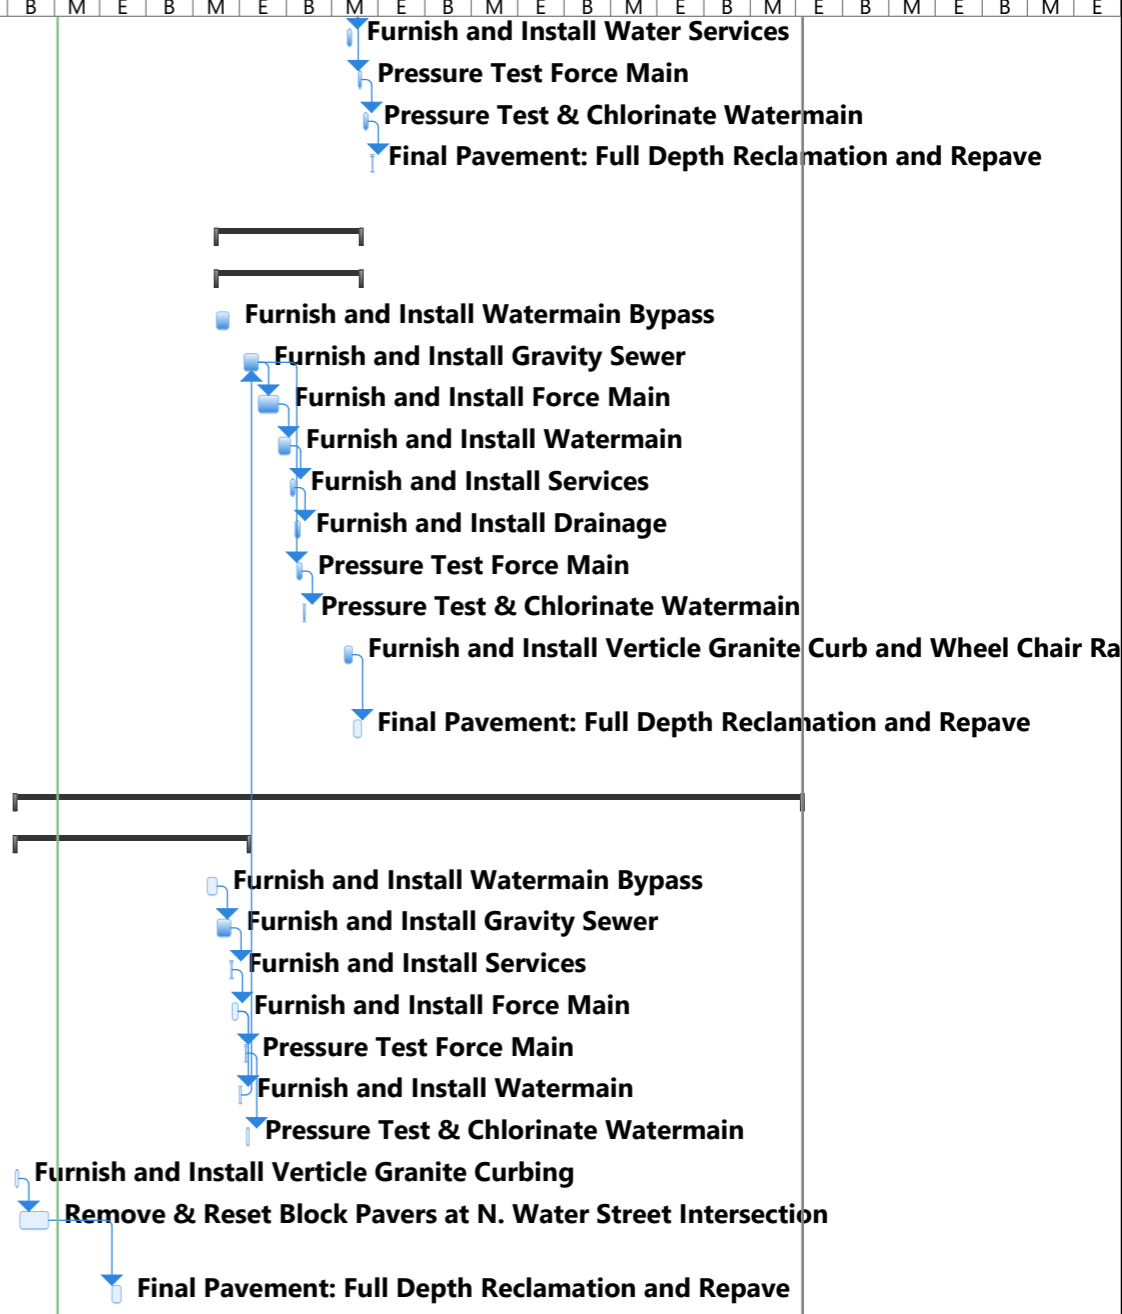

Project: Sea Street Pump Station  
Date: Wed 2/16/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Owner: Town of Nantucket  
 GC: Robert B. Our Co., Inc.  
 Engineer: Environmental Partners

Sea Street Pump Station- Force Main No. 3  
 Town of Nantucket  
 CWSRD#6722  
 Construction Schedule  
 2/15/22



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	July		December		May		October		March		August		January		June		November		April		September		February		June			
							M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M
119		Cleanup	60 days	Tue 10/1/24	Fri 12/27/24																													
120		Restoration	62 days	Tue 10/1/24	Tue 12/31/24	119SS																												
121		Punch List	30 days	Thu 1/2/25	Thu 2/13/25	120																												
122		Demobilize	30 days	Fri 2/14/25	Mon 3/31/25	121																												



Project: Sea Street Pump Station  
 Date: Wed 2/16/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
